



CHEROKEE COUNTY ROADWAY CAPITAL PROGRAM MANAGEMENT

PROJECT STATUS REPORT

June 16, 2016



CONSTRUCTION STATUS MONTHLY REPORT

6/2016

Project	Description	Contractor	Notice to Proceed	Estimated Completion Date	Current Contract Amount	Earned to Date	% Complete	Status
East Cherokee Dr at SR 20	Intersection Improvement & Traffic Signal Modification	F.E. Sims Enterprises, Inc.	7/6/2015	7/5/2016	\$ 912,565.85	\$ 251,971.70	28%	Widening SR 20 and East Cherokee Drive. Curb to be placed soon. Signal poles placed, will be hanging new signal heads after permanent road configuration
Keeter Road	Holly Street to Canton City Limit	Baldwin Paving Company, Inc.	7/13/2015	7/19/2016	\$ 1,280,129.06	\$ 451,692.22	35%	Drainage 90% complete. North end of project 50% curb placed and stone base, working on remaining subgrade and curb.
East Cherokee Dr at Lower Union Hill Road	Intersection Improvement & Traffic Signal	Bartow Paving Company, Inc.	8/26/2015	8/25/2016	\$ 654,126.43	\$ 271,023.48	41%	Curb & sidewalk installed. Asphalt placed, topping remaining. Signal poles waiting on foundation cure period.
Wyngate Parkway at Bascomb Elementary School entrance	Intersection Improvements	Chalfield Contracting, Inc.	12/14/2015	5/26/2016	\$ 376,683.43	\$ 376,683.43	100%	Project completed 5/26/2016
Kellogg Creek Rd at Woodstock Rd	Intersection Improvements	Bartow Paving Company, Inc.	1/11/2016	1/10/2017	\$ 564,638.00	\$ 28,860.43	5%	Clearing & grubbing 90% complete. CCWSA still needs to relocate water and sewer lines.
SR 92 & Robin Road TE Project	SR 92 - Woodlands Drive to Santa Fe Trail and west side Robin Road	Baldwin Paving Company, Inc.	3/7/2016	9/3/2016	\$ 410,174.88	\$ 298,525.38	73%	Project 90% complete, stamped concrete and median needs to be sprayed, punch list items need to be addressed.
East Cherokee Dr at New Dean Rusk Middle School	Intersection Improvements	Bartow Paving Company, Inc.	4/21/2016	10/18/2016	\$ 1,127,040.24	\$ 37,179.47	3%	Clearing & grubbing 10% complete. Erosion control measures installed. Utilities in process of relocating.
2016 Resurfacing Project	10 miles on various roads: portion of Bells Ferry Rd, Old Lathemtown Rd, Crowe Rd, Liberty Grove Rd, Lower Union Hill Rd, Braswell Farms, Sycamore Dr	C.W. Matthews Contracting Company, Inc.	6/8/2016	12/5/2016	\$ 2,181,823.87	\$ -	0%	Pre-construction meeting held on 5/25/2016. Beginning work on Liberty Grove Road.
Arnold Mill Road at Trickum Road	Traffic Signal Improvement	North Cherokee Electrical, Inc.	7/1/2016	9/29/2016	\$ 113,464.42	\$ -	0%	Contract sent to contractor on 6/3/2016 to be executed. Preconstruction meeting scheduled for 7/13/2016.



CONSTRUCTION STATUS MONTHLY REPORT

6/2016

Project	Description	Contractor	Notice to Proceed	Estimated Completion Date	Current Contract Amount	Earned to Date	% Complete	Status
GDOT Safety Project - Striping & Signing on 4 County Roads	Signage, Traffic Striping and Raised Pavement Marking Installation on 4 County Roadways	Peek Pavement Markings, Inc.						100% GDOT funded. Includes traffic striping and raised pavement marker installation on Bells Ferry Road, Towne Lake Parkway, Trickum Road and East Cherokee Drive. Will also include Canton Road (Woodstock City limit to Cobb County line), Wade Green Road and Eagle Drive.
Reavis Mountain	Retaining Wall Construction	TBD						Bids for construction due on 7/5/2016.
Gold Bridge Crossing over Downing Creek	Bridge overlay and sidewalk installation	TBD						Bids for construction due on 6/17/2016.
Burch Park Lane/Old Doss Lane	Construct new roadway leading to County park property	In-house by Roads & Bridges					100%	Project includes construction of a new roadway located off of Doss Road. Project complete.
Trickum Road North	Reconstruction - north of Arnold Mill Road to entrance of proposed development	In-house by Roads & Bridges					50%	Project includes correcting vertical alignment, widening, installing curb and gutter and sidewalk. Also includes adding left turn lane capacity on Arnold Mill Road eastbound at intersection. Grading complete. Curb and sidewalk construction in progress.
Puckett Creek Road	Reconstruction - SR 140 to Sam Nelson Road	In-house by Roads & Bridges					50%	Project includes pavement widening to minimum width of 20 feet, establishing a grass shoulder and ditch section, and replacement of all cross-drain pipe culverts. Grading complete. Stone base course complete.



PRE-CONSTRUCTION STATUS MONTHLY REPORT

6/2016

Project	Description	Consultant/Designer	Proposed Letting Date	Design / Pre-Construction Status	R/W Parcels (closed/req'd)	Comments
Earney Road	Roadway Reconstruction - Old Country Place to Capital City Club property	American Engineers, Inc. (AEI)		Notice to proceed issued to designer on 5/19/2016 to update plans to advertise for bids. Waiting for utilities to respond for any final plan changes.	Completed	Right-of-way acquisition complete.
Harnes Road	Roadway Reconstruction - SR 92 to Jamerson Road; includes roundabout at S. Jett Road Intersection	Atwell Group (LAI)		Project design is approximately 90% complete. Need to complete drainage analysis, drainage design, erosion control plans and right-of-way plans.	0/52	Will take approximately 2 months to complete project design.
East Cherokee Dr at Old Hwy 5	Intersection Improvements	American Engineers, Inc. (AEI)	August 2016	Right-of-way acquisition is in progress. Plans being revised as a result of right-of-way negotiations. Four parcels still in negotiation - possible condemnations. Waiting on markups from CCWSA. All other utility conflicts have been addressed.	17/21	Project will include dual left turn lanes from Old Hwy 5 to East Cherokee Dr eastbound, and also dual left turn lanes from East Cherokee Dr to Old Hwy 5 southbound. Project also includes right turn lane from East Cherokee Dr to Mill Creek Rd. Additional receiving lanes also included on East Cherokee Dr and Old Hwy 5.
East Cherokee Dr at SR 140	Intersection Improvements & Traffic Signal Modification	AMEC, Inc. & Moreland-Allobelli Assoc, Inc. (MAAI)	Late 2017	Plans updated to meet current GDOT and EPD ES&PC standards. MAAI is working on environmental document - expected to be complete June 2016. Requires a full CE - Categorical Exclusion that needs approval from FHWA. Waiting on updates from utility companies.	0/19	Project includes providing right-turn lanes on all quadrants of intersection. GDOT has committed to fund \$1,000,000 of construction cost dependent upon approval of environmental document.
Hickory Rd at Stringer Rd/ Carriage Ln	Intersection Improvements	American Engineers, Inc. (AEI)	TBD	Preliminary plans have been submitted to County and are under review. Designer given notice to proceed to add traffic signal to project on 5/19/2016. Waiting on utilities to respond.		Project includes construction of left turn lane and traffic signal on Hickory Road to serve Stringer Road and Carriage Lane. Also includes vertical realignment of Hickory Road at intersection - cut.
Stringer Road at SR 140	Intersection Improvements	Croy Engineering	TBD	Design proposals received on 5/26/2016. Design contract to be awarded at 6/21/2016 BOC meeting.		Project includes construction of an exclusive right-turn lane from Stringer Road to SR 140.
Bells Ferry Road at Ridge Road	Intersection Improvements & Traffic Signal	AECOM	TBD	Plans currently being updated to meet current GDOT and EPD ES&PC standards. Updated plans under review.	0/10	Project includes realignment of intersection, installation of a traffic signal and installation of a left-turn lane from southbound Bells Ferry Road to Ridge Road.
Trickum Road at Jamerson Road	Intersection Improvements	AECOM	Fall 2016	Plans currently being updated to meet current GDOT and EPD ES&PC standards. Updated plans are complete. Notice to proceed with right-of-way acquisition issued on 6/16/2016.	0/13	Project includes installation of right-turn lane from southbound Trickum Road to Jamerson Road and providing additional left-turn lane storage from southbound Trickum Road to Jamerson Road.
Lower Burris Rd/Puckett Creek Rd at SR 140	Intersection Improvements & Traffic Signal	Clark Patterson Design	TBD	Vertical profile on Lower Burris Rd to be modified so that the adjacent pump house will not be impacted. Updated plans submitted on 6/10/2016 for review.	0/8	Project includes installation of left-turn lanes and a traffic signal on SR 140 at Lower Burris Road and Puckett Creek Road.
East Cherokee Dr at Tripp Road	Intersection Improvements	Pond & Company	TBD	Construction and right-of-way plans complete. Design contract to update plans to current GDOT and EPD ES&PC standards to be awarded at 6/21/2016 BOC meeting.		Project includes realignment of intersection of Tripp Road and East Cherokee Drive and installation of a southbound left-turn lane from East Cherokee Drive to Tripp Road.
East Cherokee Drive at South Holly Springs Rd/Thornwood Dr.	Intersection Improvements	AECOM	TBD	Construction and right-of-way plans complete. Design contract to update plans to current GDOT and EPD ES&PC standards to be awarded at 6/21/2016 BOC meeting.		Project includes providing left-turn lanes and deceleration lanes on East Cherokee Drive for both South Holly Springs Road and Thornwood Drive.
Bells Ferry Road South of Steels Bridge Road	Intersection Improvements - Improve sight distance on NB approach to Bells Ferry Rd/Steels Bridge Intersection	Atwell Group (LAI)		Construction and right-of-way plans complete.		Project on hold. Development of adjacent commercial parcels on hold. Will require substantial construction staging to keep open to traffic. Plans will need updating.
Trickum Road at Wagon Trail/Trickum Hills Dr	Intersection Improvements	Keck & Wood, Inc.		Construction and right-of-way plans complete.		Project on hold. Plans will need updating. Project includes providing a center left turn lane for both side roads. Also includes vertical realignment to improve sight distance. Several utility conflicts are anticipated - CCWSA water main and City of Woodstock water main. May have to close roadway in order to complete the vertical realignment.



PRE-CONSTRUCTION STATUS MONTHLY REPORT

6/2016

Project	Description	Consultant/Designer	Proposed Letting Date	Design / Pre-Construction Status	R/W Parcels (closed/req'd)	Comments
Sixes Road at Gresham Mill Parkway	Intersection Improvements - Traffic signal installation	A&R Engineering		Traffic signal design 90% complete.	0	Update of existing traffic signal design. County has the signal poles in storage. Plan will be updated to current GDOT standards and flashing yellow operation.
East Cherokee Dr at Gaddis Rd/Chadwyck Ln	Intersection Improvements	American Engineers, Inc. (AEI)	TBD	Preliminary plans have been submitted and approved. Right-of-way plans under review. Waiting on utilities to respond and show potential conflicts.		Project includes construction of a roundabout at the intersection.
SR 92 at Ragsdale Rd/Claremore Dr	Intersection Improvements	Southeastern Engineering, Inc. (SEI)	TBD	Design completed. Signal design sent to GDOT for review and approval. Right-of-way acquisition in progress.	0/4	Project includes expanding intersection to include dual left turn lanes, dedicated through lane and dedicated right turn lane on southbound approach of Ragsdale Rd to SR 92. Also includes adding dedicated left turn lane on Claremore Dr.
SR 92 at 3 locations - Operational Improvements	Intersection Improvements	Southeastern Engineering, Inc. (SEI)	TBD	Design completed. Waiting on GDOT approval of signal modifications. Right-of-way acquisition in progress at Woodstock Road intersection.	0/2	Project includes adding dedicated right turn lane on southbound approach of Woodstock Rd to SR 92; adding dedicated right turn lane on southbound approach of Robin Rd to SR 92 with possibly re-striping; providing southbound transition for dual left turn lanes and possibly adding dual northbound left turn lanes at Bells Ferry Rd and SR 92. All work done inside right-of-way.
Batesville Road at Lower Birmingham Road	Intersection Improvements	BM&K Construction & Engineering, Inc.	TBD	Notice to proceed with design issued on 3/18/2016. Concept drawings submitted 6/10/2016 for review and approval.		Project includes adding dedicated left turn lane on eastbound Batesville Rd to northbound Lower Birmingham Rd, adding dedicated right-turn and left-turn lane from southbound Lower Birmingham Rd to Batesville Rd.
SR 140 at Darnell Road	Intersection Improvements	BM&K Construction & Engineering, Inc.	TBD	Notice to proceed with design issued on 3/18/2016. Concept drawings submitted 6/10/2016 for review and approval.		Project includes adding left-turn lane from westbound SR 140 to Darnell Road.
Canton Road Sidewalk Project	Installation of sidewalk on west side of Canton Road from Cobb Co line to Stockwood Drive	Moreland-Altobelli (MAAI)	Fall 2017	Field survey and environmental assessment have been completed. Awaiting approval of environmental document. Preliminary construction plans have been submitted to GDOT. Addressing responses to construction plans and anticipate completion in 45 days. Right-of-way acquisition scheduled for October 2016.		Project is 80% federally funded, designed per GDOT PDP. Concept report has been approved.
Arborview Parkway Sidewalk & Drainage Improvement Project	Installation of sidewalk and storm drainage on north side of Arborview Pkwy from Woodstock Rd to amenity area.	Integrated Science & Engineering, Inc. (ISE)	Fall 2016	Preliminary plans have been submitted to the County. Designer currently working on a Cobb County Water System sewer force main conflict on the project.		Project will correct drainage problem occurring at subdivision amenity area and also provide a sidewalk to amenity area from Woodcreek subdivision located on west side of Woodstock Road.
Bells Ferry Road - Southfork Way to Victoria Road	GDOT Designed and Funded Roadway Improvements: STP 1375 (5) GDOT Project P.I. 630977	McGee Partners	2018	GDOT restarted design phase. Survey is complete. GDOT has kicked off design of project.	141	GDOT design and construct. County to acquire right-of-way. Project limit revised to end at Victoria Road.
Bells Ferry Road over Little River/Lake Allatoona	GDOT Designed and Funded Bridge Project: BRSTP 1375 (6) GDOT Project P.I. 630975	McGee Partners	2018	GDOT restarted design phase. Survey is complete. Using current environmental consultant - McGee Partners to develop new concept report. GDOT has kicked off design of project.		GDOT design and construct. County to acquire right-of-way. GDOT working to bid with Bells Ferry Road project. County will look at possibility of advanced acquisition of restaurant parcel.
Countywide Traffic Signal Upgrade and Timing Project	GDOT designed and funded intersection improvements - traffic signal upgrades and timing at 42 intersections.	VH&B		Inventory and design are complete. GDOT will issue task orders on various work items to be completed.		GDOT design and manage construction using state contractors.
Little Road	Widening and improvements - Hickory Road to Vaughn Road	Moreland-Altobelli (MAAI)		The ES&PC plans revised and submitted to EPD. NTP with redesign by MAAI on 8/19/2015. Field work is complete for the Little Road property resolution. Preliminary plans 80% complete.	0/21	Plans originally designed in-house. An EPD stream buffer variance and an ACOE Nationwide permit for stream impacts have both been obtained in summer 2014.


KEETER ROAD



EAST CHEROKEE DRIVE AT LOWER UNION HILL ROAD




EAST CHEROKEE DRIVE AT DEAN RUSK MIDDLE SCHOOL

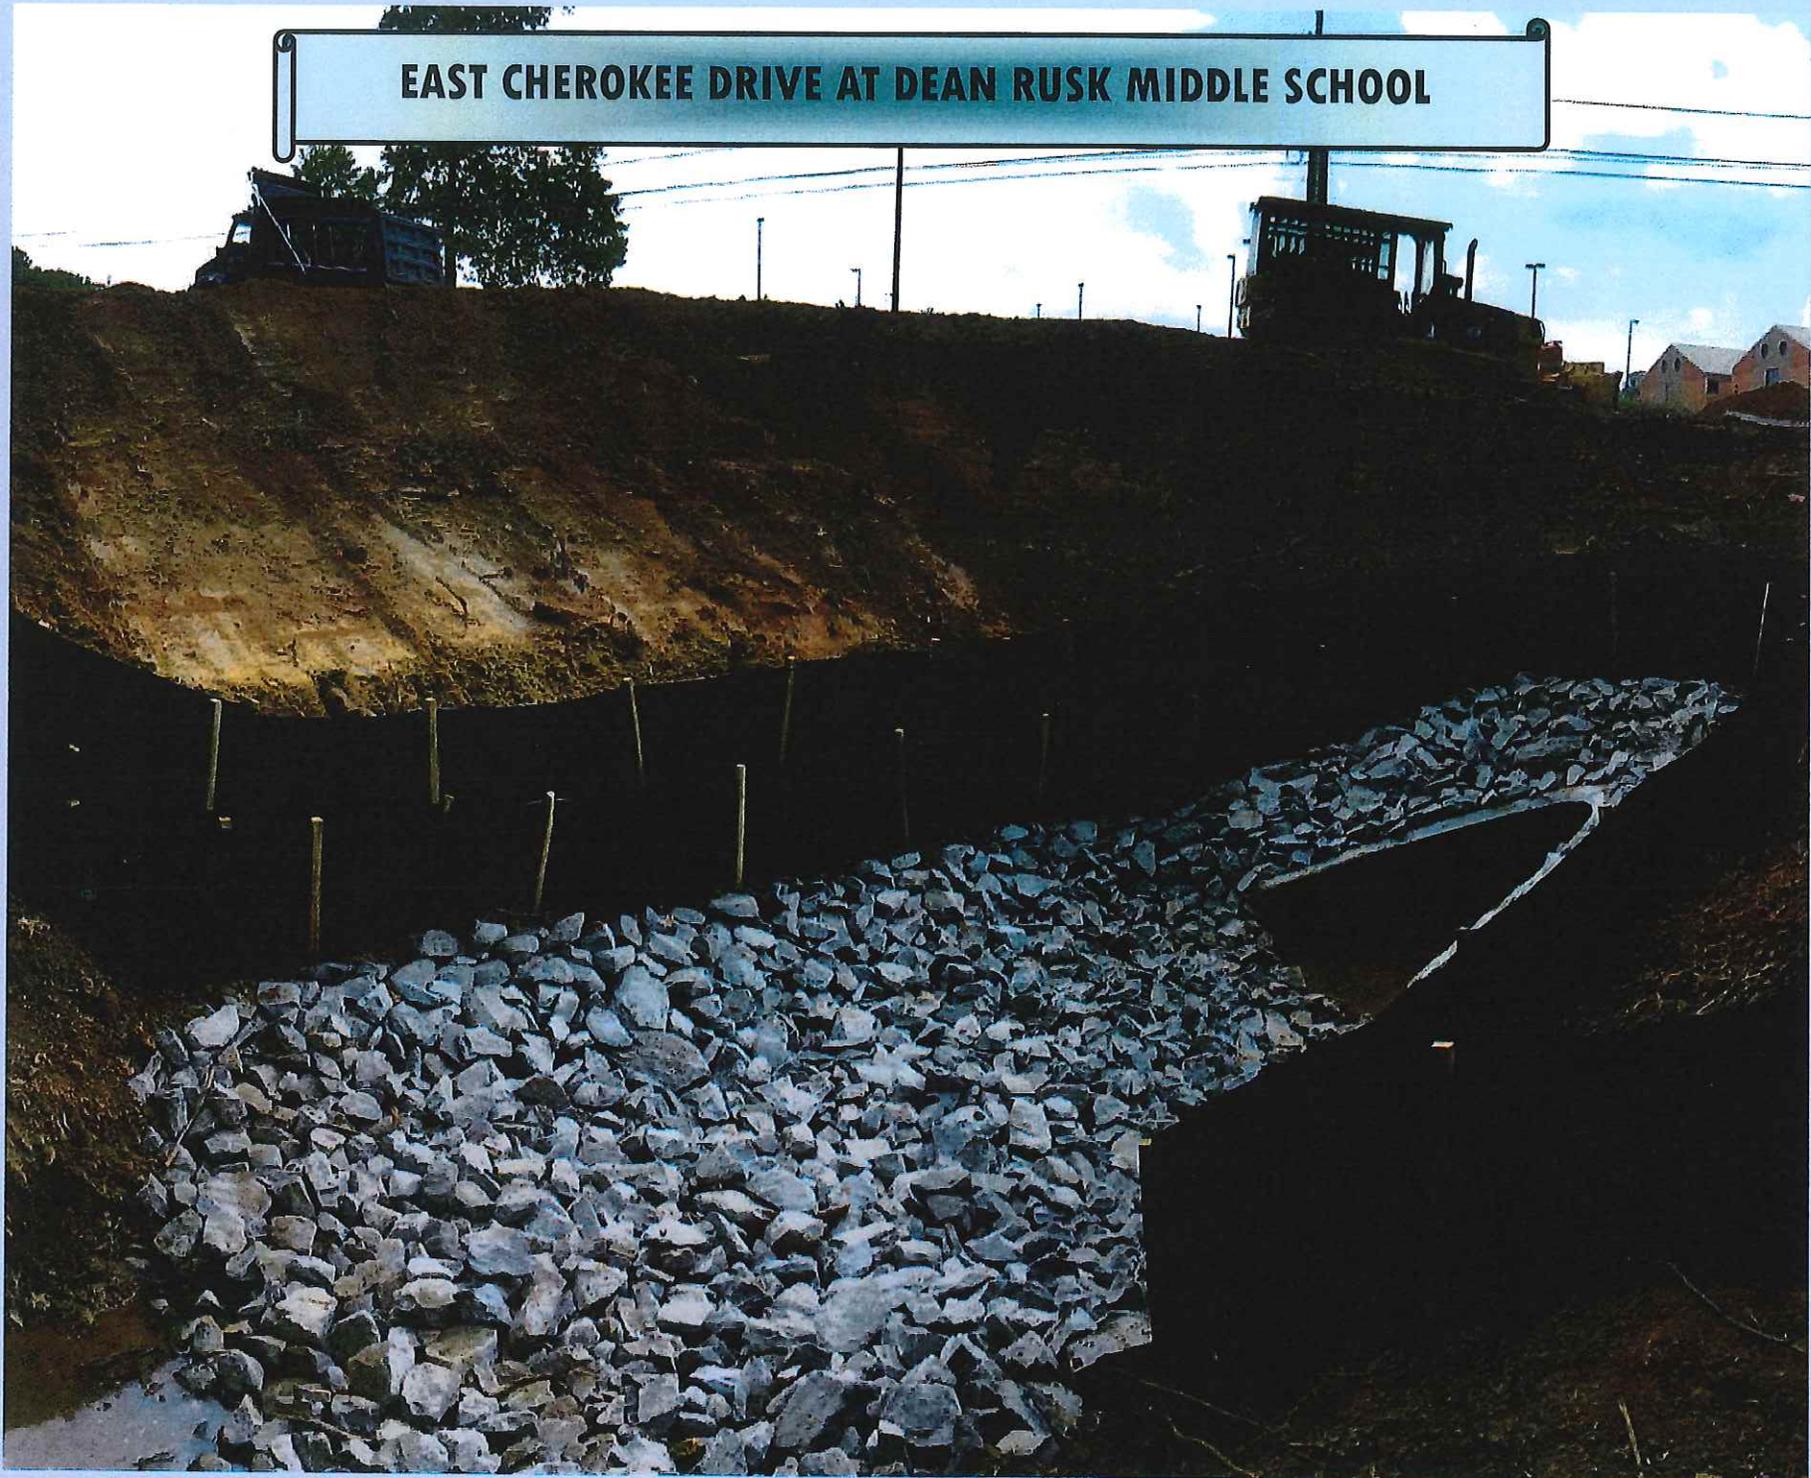


EAST CHEROKEE DRIVE AT SR 20



KELLOGG CREEK ROAD AT WOODSTOCK ROAD

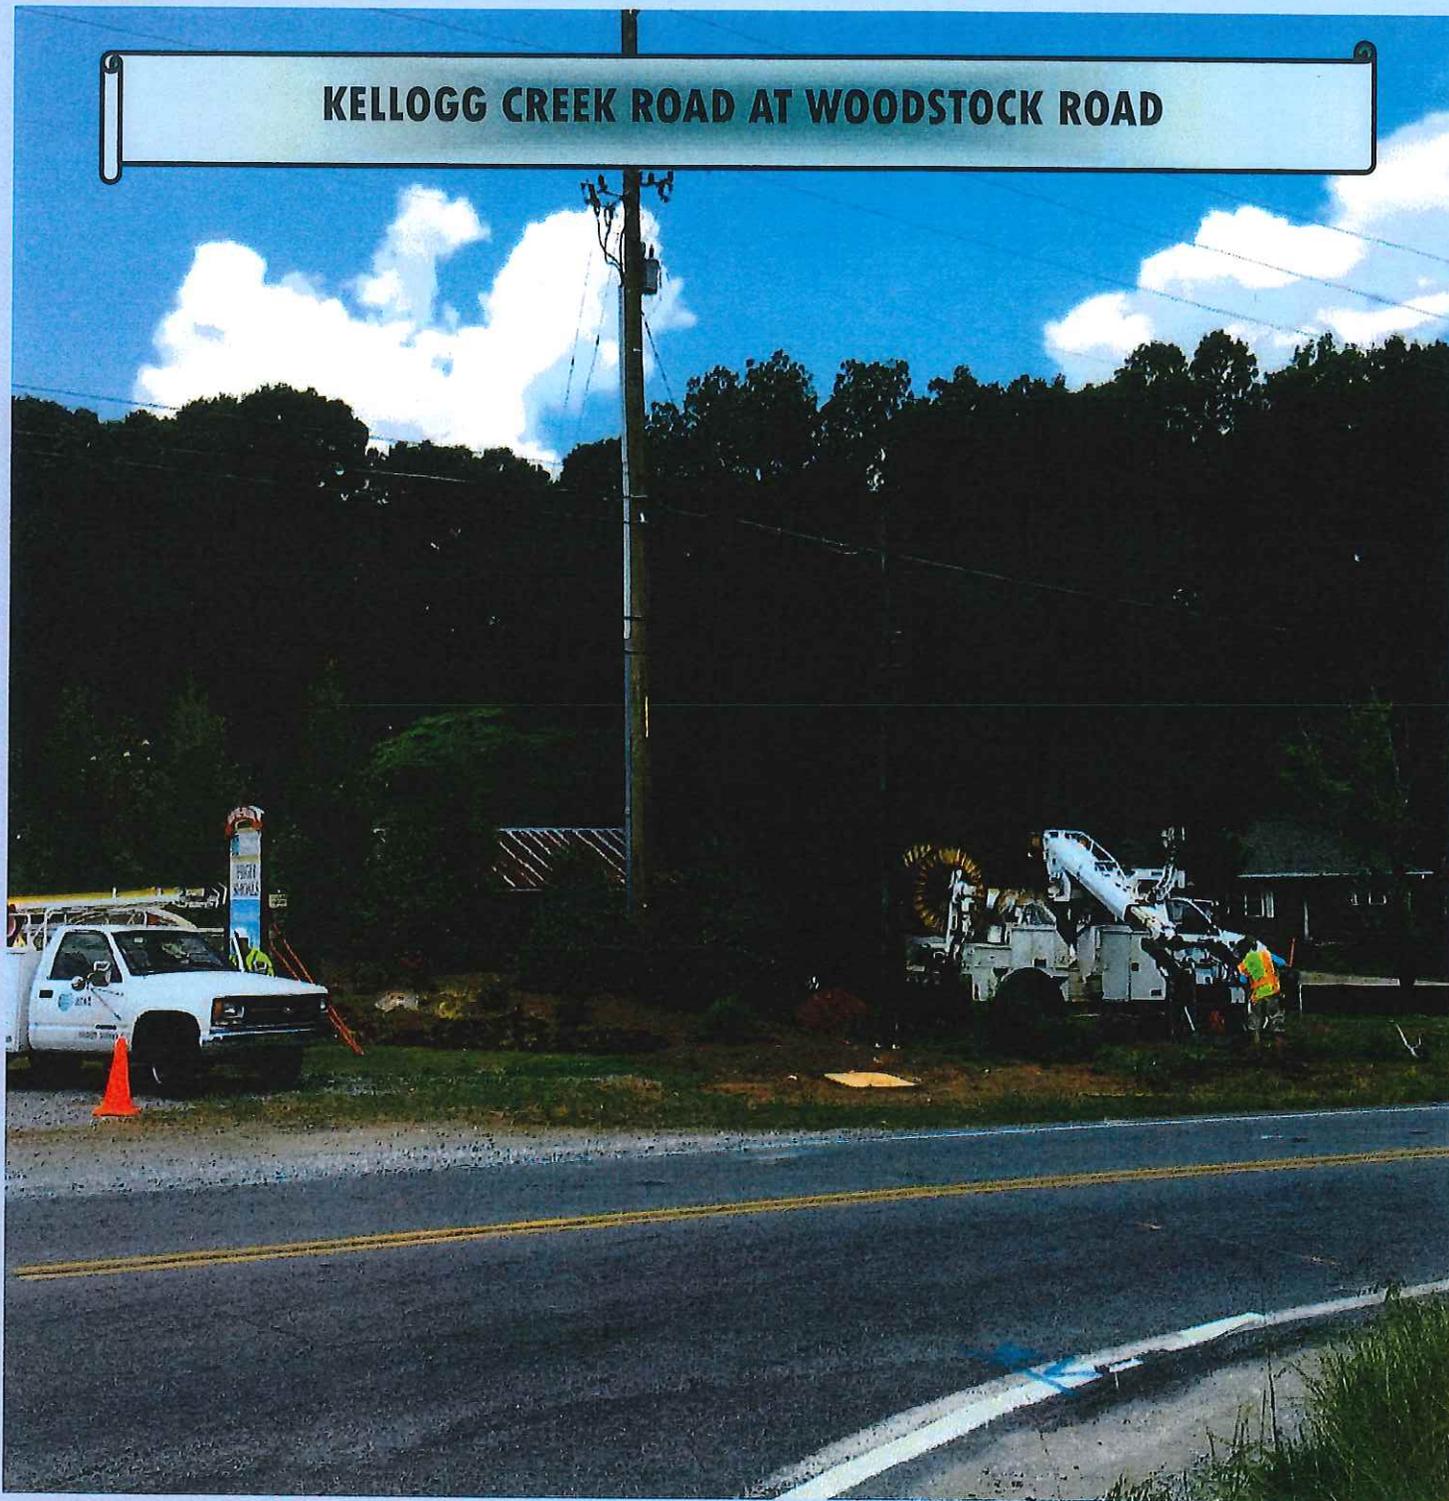

SR 92 AT ROBIN ROAD

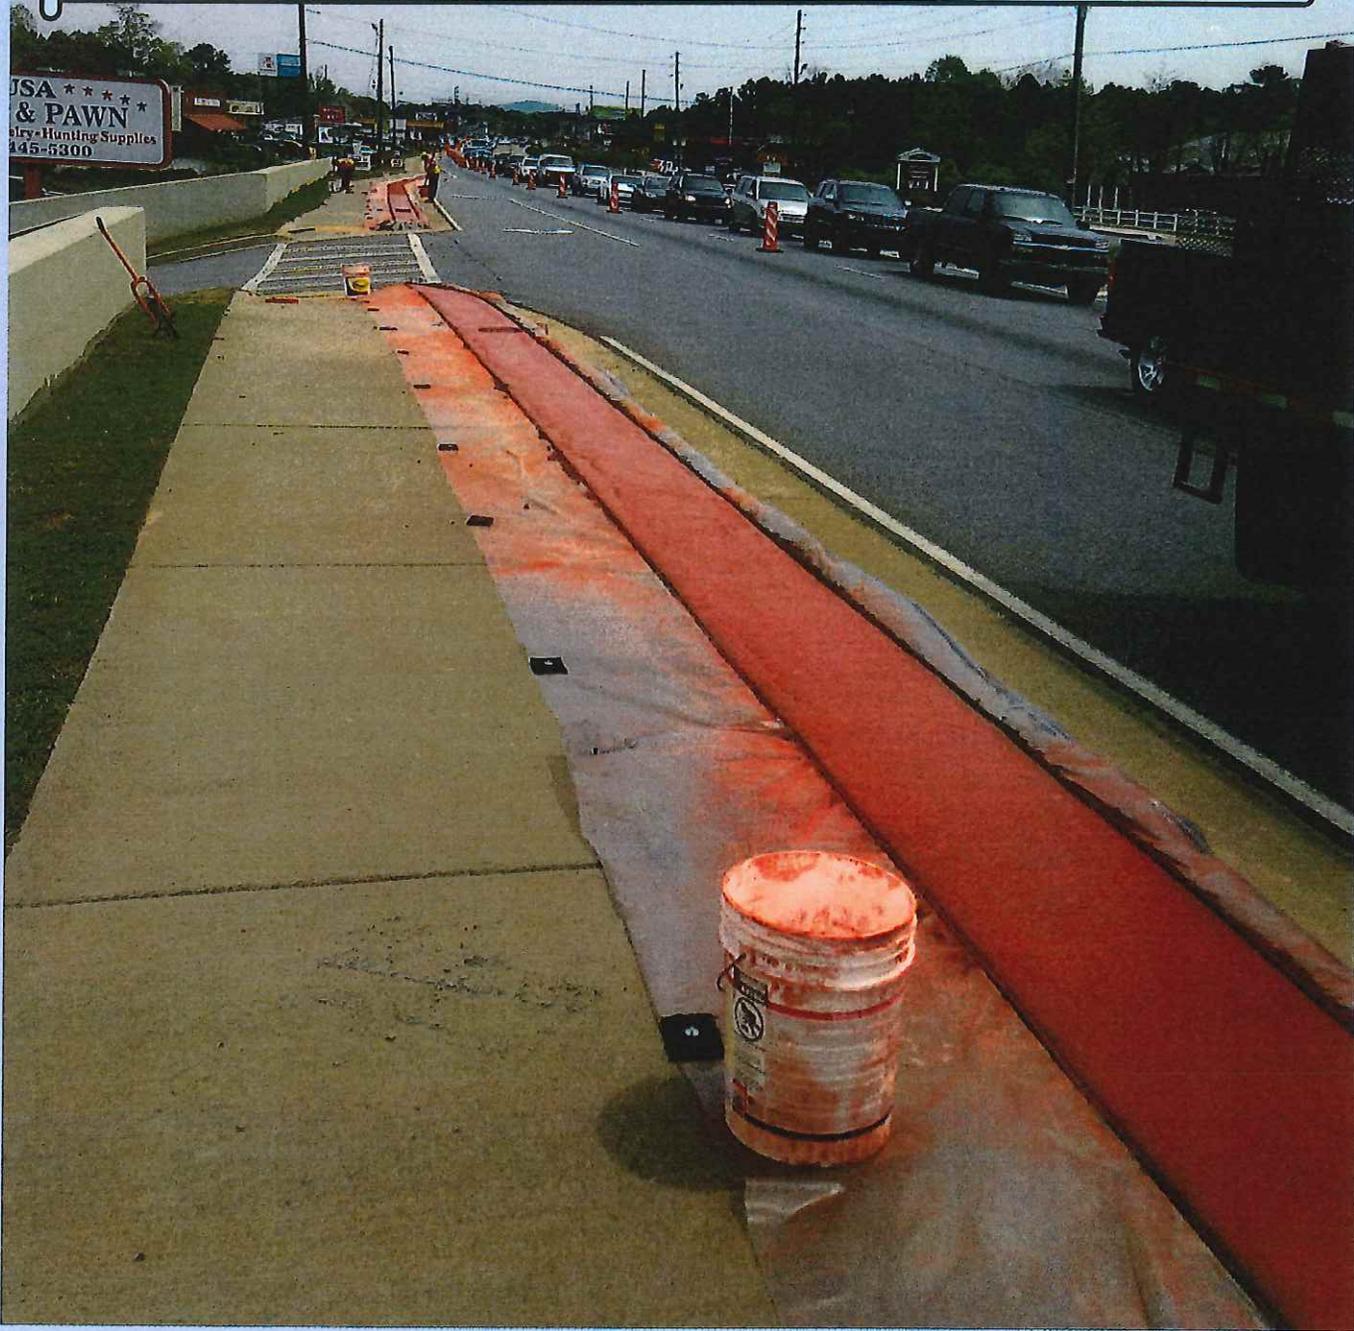

WYNGATE PARKWAY AT BASCOMB ELEMENTARY SCHOOL

