

SEPTEMBER 15, 2011

CHEROKEE COUNTY CAPITAL PROGRAM MANAGEMENT

PROGRESS REPORT

PRECONSTRUCTION STATUS REPORT

PROJ NO.	PROPOSED ADVERTISE DATE	PROPOSED LETTING DATE	DESIGN / PRECONSTRUCTION STATUS COMMENTS	R/W PARCELS	COMMENTS
----------	-------------------------------	-----------------------------	---	----------------	----------

CONSTRUCTION PLANS COMPLETE

ROADWAY IMPROVEMENTS

Earney Road Old Country Place to CCC Dam	Reconstruction		American Engineers designer. Construction and right of way plans complete. Right of way acquisition complete.		Project on hold. Possible construction by Roads & Bridges.
East Rope Mill Road	Reconstruct to meet 30 MPH speed design		American Engineers designer. Construction and right of way plans complete.		Project on hold. Property owners talking about combining parcels and realigning roadway.
Hames Road/South Jett Rd	Reconstruction		Hames Rd. - Construction plans complete. South Jett Rd. - Construction plans complete. Finalizing R/W acquisition.		Project on hold. Some Right-of-way acquisition still remains.
Ragsdale Road	Reconstruction		Delon Hampton & Assoc designer. Construction plans complete. Right of way acquisition complete.		Project on hold. Roads & Bridges may construct.
Steel Bridge Rd	Widening		LAI Engineering, designer. Construction plans complete. Right of way acquisition complete.		Project on hold. Roads & Bridges may construct. Plans updated to reflect new subdivision entrance.
Wiley Bridge Road EPR 398 (057)	Reconstruction		Delon Hampton & Assoc designer. Southern R/W - R/W acquisition.	118 Closed:56 Negotiate:17	Project on hold.

INTERSECTION IMPROVEMENTS

Bells Ferry Road South of Steels Bridge Rd	Imprv Sight Distance on NB approach to Bells Ferry Rd/Steels Br Inter		LAI Engineering designer. Construction and right of way plans complete.		Project on hold. Development of commercial parcels on hold.
Bells Ferry Road @ Ridge Road	Intersection Imprv. & Traffic Signal Design		URS Corp. designer. Construction and R/W plans complete.	10 Parcels	Project on hold. Data Book for right of way acquisitions is complete.
East Cherokee Dr @ Lower Union Hill Road	Intersection Improvements		URS Corp. designer. Construction and R/W plans complete.		Project on hold. Development on hold. Developer to pay for installation of traffic signal and part of intersection. Developer agreement is in place.
East Cherokee Dr @ SR 20	Intersection Improvements		STV/Ralph Whitehead & Assoc. designer. Construction & R/W plans complete.		Project on hold.
East Cherokee Dr@Tripp Rd	Intersection Improvements		Pond & Company designer. Construction and R/W plans complete.		Project on hold.

PRECONSTRUCTION STATUS REPORT

ROAD NAME	PROJ NO.	PROPOSED ADVERTISE DATE	PROPOSED LETTING DATE	DESIGN / PRECONSTRUCTION STATUS	COMMENTS	R/W PARCELS	COMMENTS
-----------	----------	-------------------------------	-----------------------------	------------------------------------	----------	----------------	----------

CONSTRUCTION PLANS COMPLETE

INTERSECTION IMPROVEMENTS (Cont'd.)

Kellogg Cr Rd @ Woodstock Rd	Intersection Improvements			Wolverton Assoc. designer. Construction & R/W plans complete. Right of way acquisition is complete.			Project on hold. Development on hold. Developer agreement is in place.
SR 140/Lower Burris Rd/Puckett Cr Rd	Intersection Improvement			Ross Consulting Engr. Designer. Construction and R/W plans complete.			Project on hold.
Trickum Road @ Jamerson Road	Intersection Improvements			URS Corporation designer. Construction and R/W plans complete.			Project on hold. Look at possibly adding to Cobb County Jamerson Road project.
Trickum Road @Wagon Trail/Trickum Hill Dr	Intersection Improvements			Keck & Wood designer. Construction and R/W plans complete.			Project on hold.
East Cherokee Drive/South Holly Springs Rd/Thornwood Dr.	Intersection Improvement			URS Corp. designer. Construction and right of way plans complete.			Project on hold.
SR 140 @ East Cherokee Dr.	Intersection Improvement			Mactec, Inc. designer. Construction and right of way plans complete.			Project on hold.

PRECONSTRUCTION STATUS REPORT

ROAD NAME	PROJ NO.	PROPOSED ADVERTISE DATE	PROPOSED LETTING DATE	DESIGN / PRECONSTRUCTION STATUS COMMENTS	R/W PARCELS	COMMENTS
DESIGN PROJECTS						
ROADWAY IMPROVEMENTS						
Bells Ferry Rd Southfork Way - Little River Bridge	STP 1375 (5) GDOT Project P.I. 630977			GDOT design & const. Cherokee Co. to acquire R/W. GDOT has proj. on hold. Proj. limits being revised to end at Victoria Rd. Awaiting final review by FHWA.	141	Reviewed the VES report from DHA & sent comments back to GDOT 12/21/07. New Project Manager at GDOT to possibly restart design in late 2011.
INTERSECTION IMPROVEMENTS						
East Cherokee Dr. @ Old Highway 5	Intersection Improvement			American Engineers, Inc., designer.		Working on completing final plans and right of way plans.
BRIDGES						
Bells Ferry Rd over L. River/Lake Allatoona	BRSSTP 1375 (6)			GDOT designer. County to buy R/W. GDOT working at bidding with Bells Ferry Road Project. GDOT has placed design on hold.		New Project Manager at GDOT to possibly restart design in late 2011.
Tripp Road	Bridge Repair			AECOM is working on plans to construct bridge abutment repairs.		Design being finalized in accordance with geotechnical report results.

1% CONSTRUCTION STATUS REPORT

PROJ NO.	PROJECT DESCRIPTION	CONTRACTOR	NOTICE TO PROCEED	COMPLETION DATE	CURRENT CONTRACT AMOUNT	EARNED TO DATE	PERCENT COMPLETE	COMMENTS
BRIDGE PROJECTS								
Howell Br Rd Bridge @ Sharp Mtn Creek	Bridge Replacement	Sunbelt Structures	-	-	\$1,443,800.00	-	-	Trees planted December 2010 - first growing season.
ROADWAY CONSTRUCTION								
Cherokee County Soccer Complex	Construct & install access rds, parking lots & soccer fields	F.E. Sims Enterprises, Inc.	03/02/09	180 Cal Days *	\$3,328,246.16	\$3,119,939.00	95.00%	Project complete. Working on settlement with Sims on grassing.
Priest Rd/Hunt Rd Connector	Grading, Drain, Base & Paving, Culvert	Sunbelt Structures	04/26/10	300 Cal Days	\$2,197,433.66	\$2,233,978.00	95.00%	Pay items complete. Punch List complete except for paving @ school drive.
Wade Green Rd	Landscaping & Enhancements	Butch Thompson Enterprises, Inc.	02/05/10	180 Cal Days	\$207,866.94	\$167,611.00	95.00%	Final inspection & payment after 10/15/11.

1% CONSTRUCTION STATUS REPORT

PROJ NO	PROJECT DESCRIPTION	CONTRACTOR	NOTICE TO PROCEED	COMPL DATE	CURRENT CONTRACT AMOUNT	EARNED TO DATE	PERCENT COMPL	COMMENTS
ROADS & BRIDGES PROJECTS								
2011 LARP S012948 - LAR	14 various Co rds 12.59 miles resurfacing							100% Complete. Needs minor striping.
2011 LMIG S013190-PR								100% Complete. Needs minor striping.
Epperson Road								Project complete. Awaiting stand of grass.
Roscoe Collett Court								Construction and Erosion Control plans complete. Dennis has easements for plans.
Roscoe Collett Road								Construction and Erosion Control plans complete. Dennis has easements for plans.
Upper Sweetwater Trail	Woodall Rd eastward to Sisley Trl - 2500 Ft.							Clearing complete.




Priest Rd/Hunt Rd Connector

09/14/2011 09:53



Bells Ferry Rd @ Towne Lake Pkwy

09/14/2011 11:24

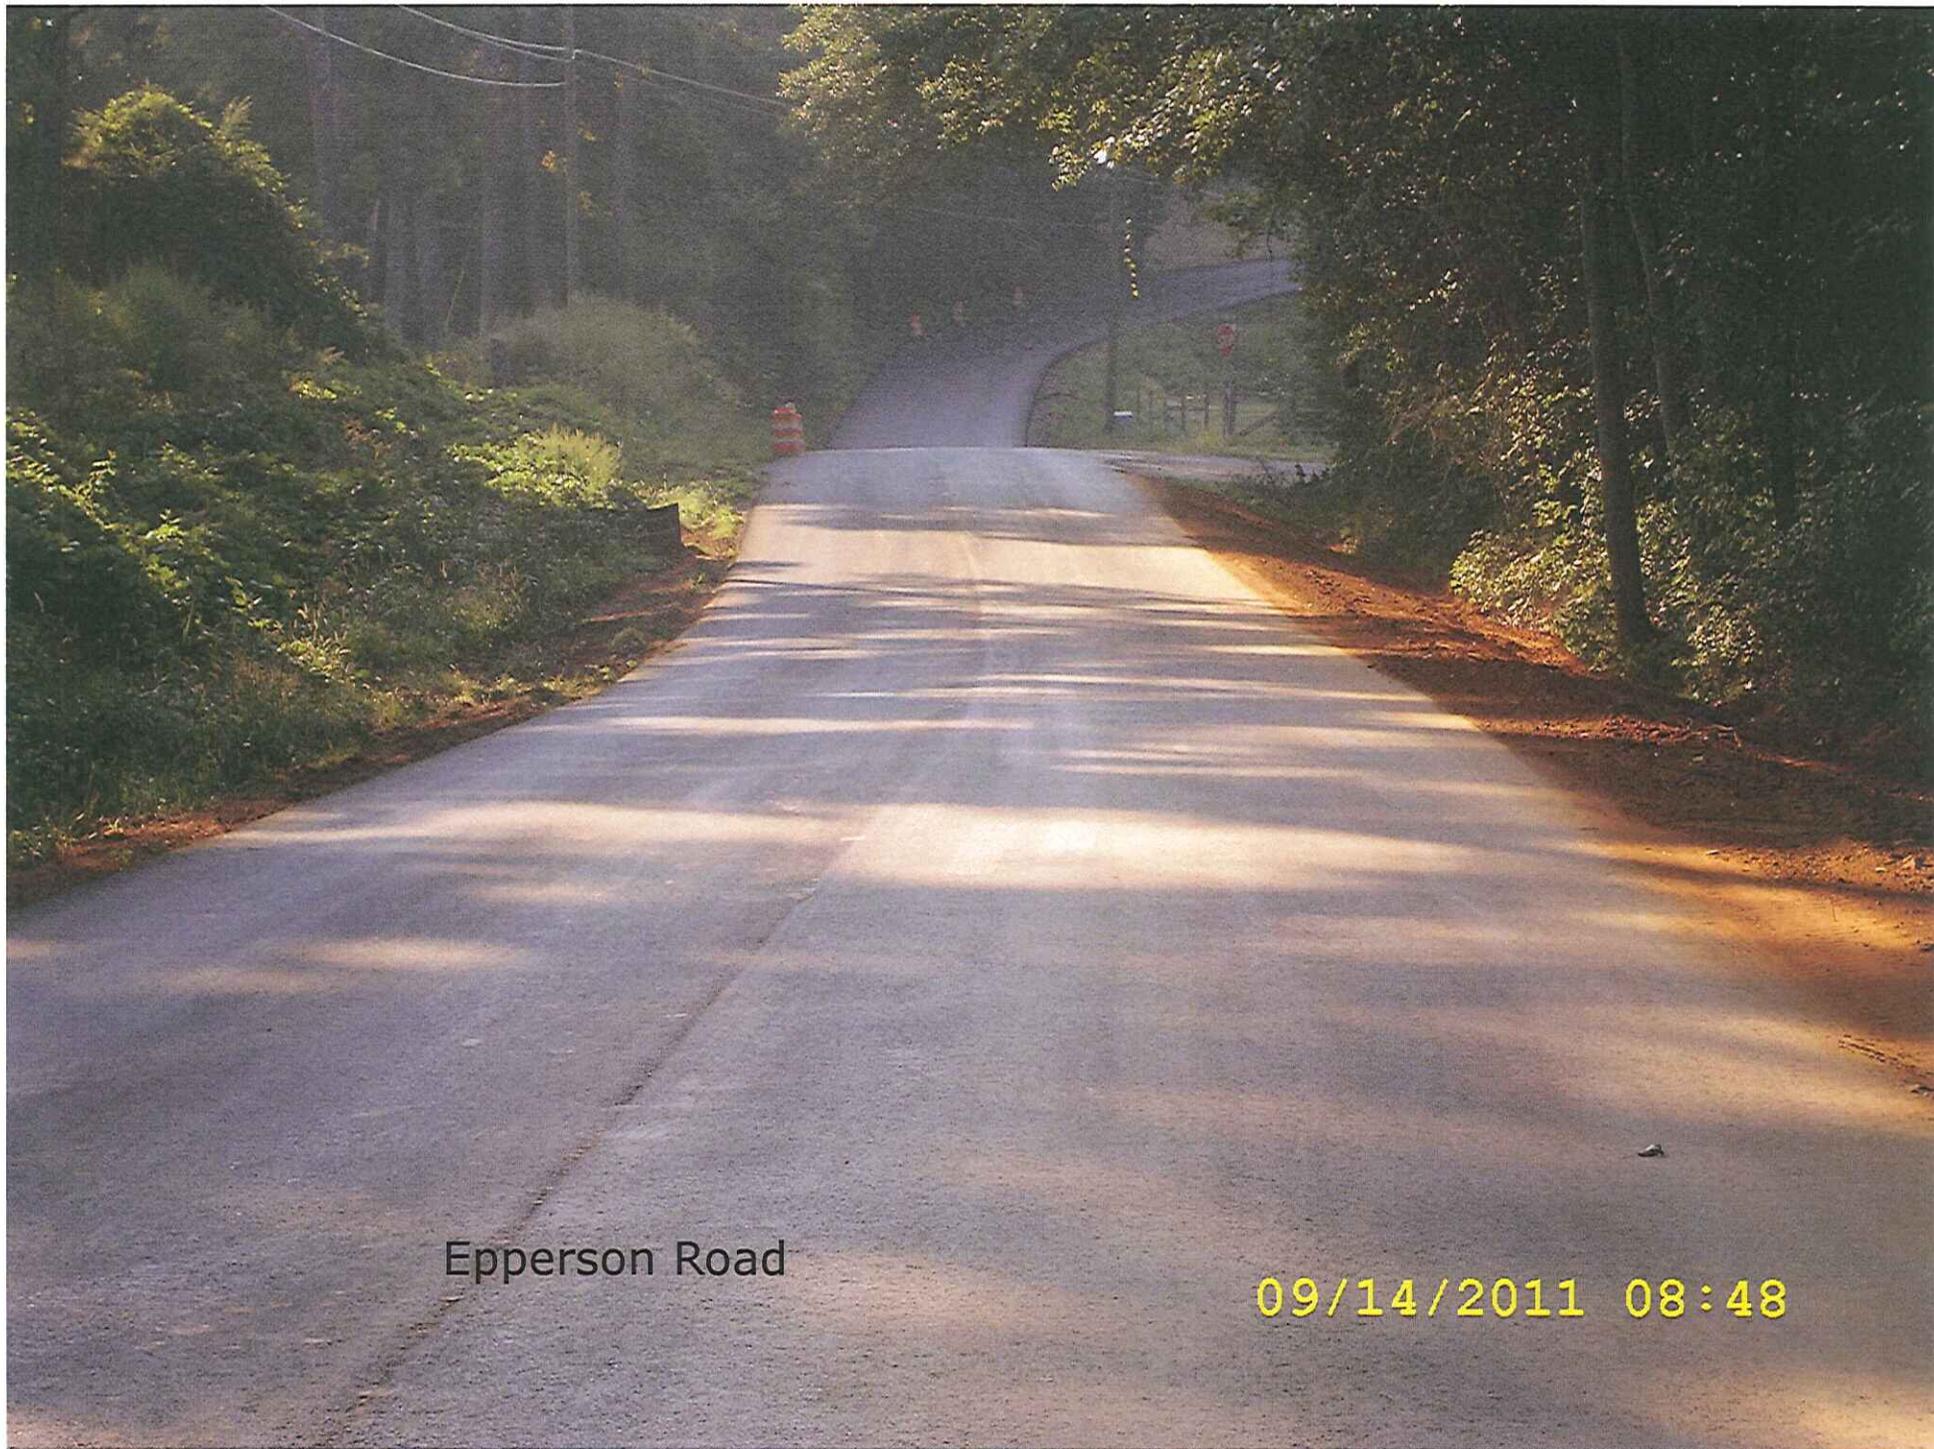

Epperson Road

09/14/2011 08:48
